


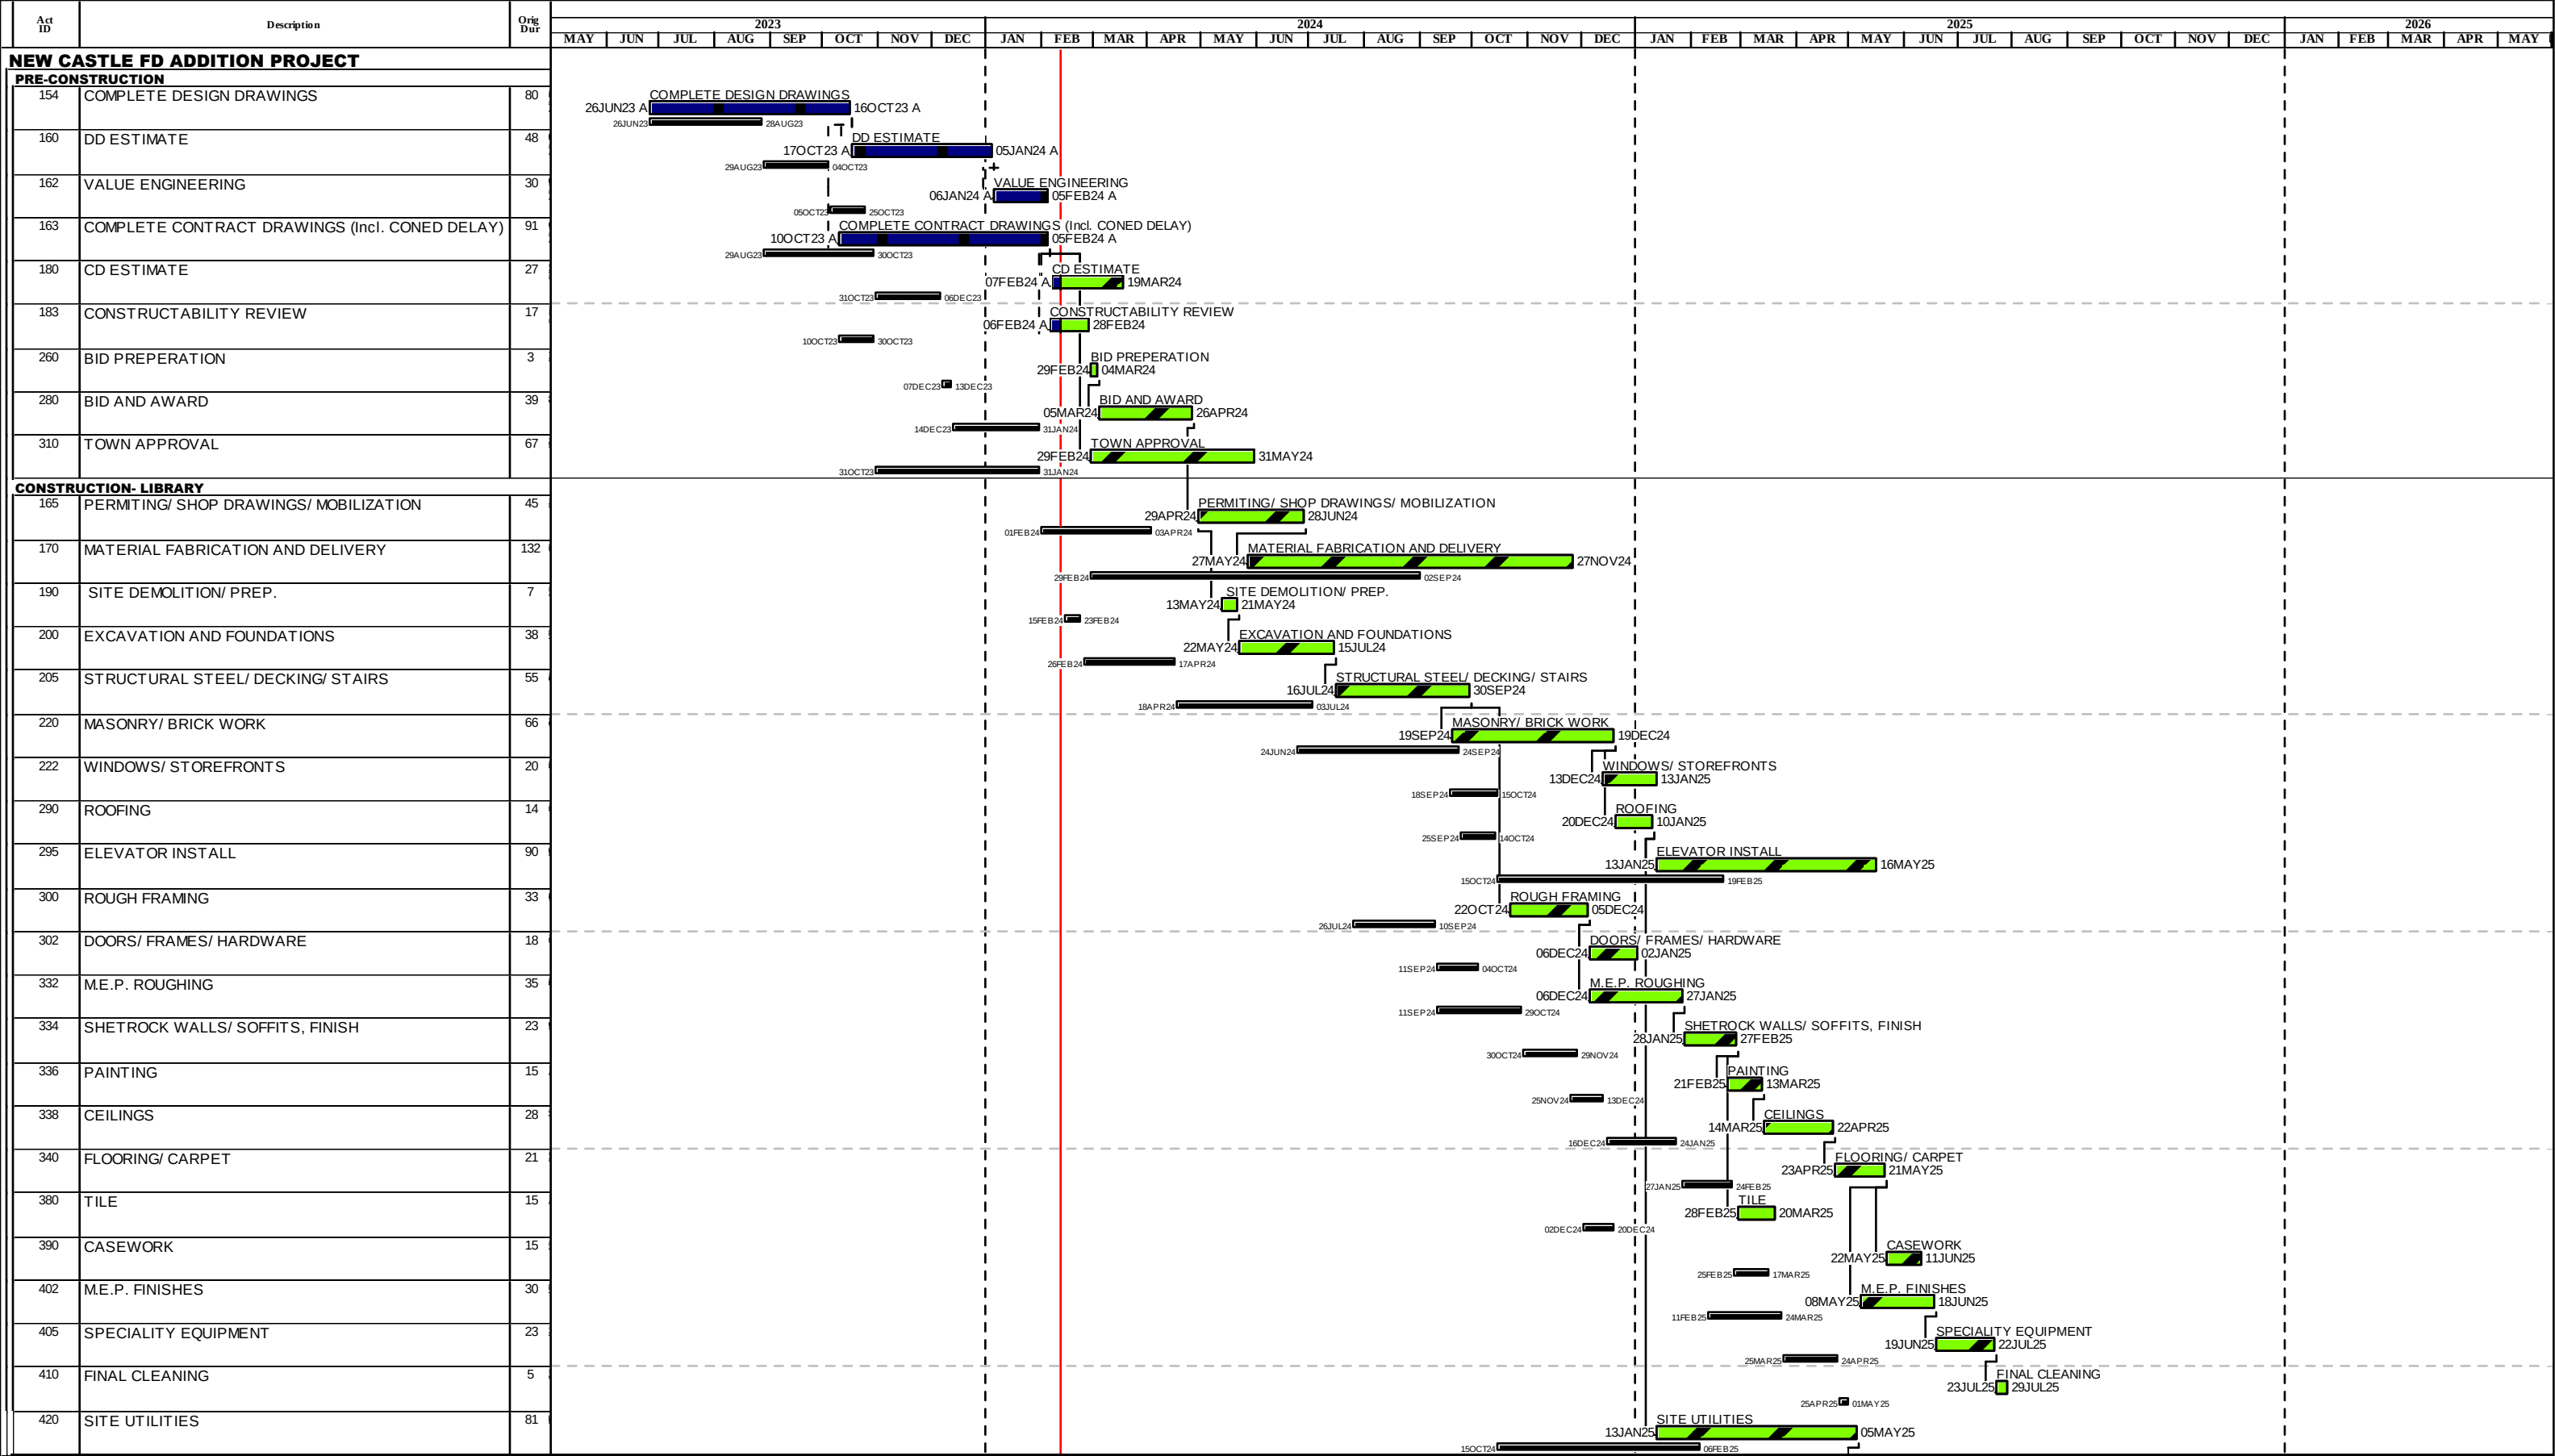

Company name	Triton
Project name	New Castle FD M...
Project title	New Castle FD
Run date	07FEB24
Number/Version	Master 8 1-15-24
Page number	1A
© Primavera Systems, Inc.	

NEW CASTLE FIRE DISTRICT NO. 1

MASTER SCHEDULE

- Early bar
- Target bar
- Progress bar
- Critical bar
- Summary bar
- Start milestone point
- Finish milestone point

	Act ID	Description	Orig Dur	2023												2024												2025												2026									
				MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY									
	440	SPECIALITY EQUIPMENT	23																									07FEB25  11MAR25												SPECIALITY EQUIPMENT 06MAY25  05JUN25									
	443	PARKING LOTS/CURBS/ SIDE WALKS	37																									12MAR25  01MAY25												PARKING LOTS/CURBS/ SIDE WALKS 06JUN25  29JUL25									
CLOSE OUT																																																	
	250	SUBSTANTIAL COMPLETION-	0																									01MAY25 												SUBSTANTIAL COMPLETION- 29JUL25 									
	270	PUNCH LIST/ CLOSE OUT-	44																									02MAY25  02JUL25												PUNCH LIST/ CLOSE OUT- 30JUL25  29SEP25									
